


Quarterly Executive Summary
Auditorium Lighting Retrofit – Myrtle Beach High School
Q2 2019



New House Lights

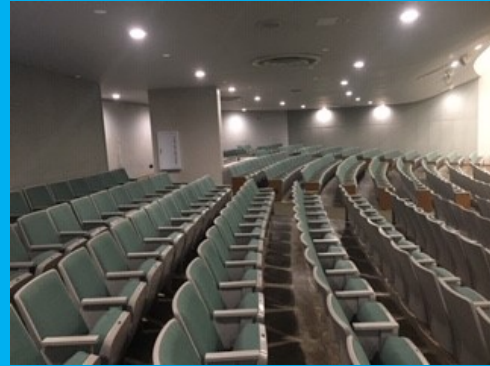

Lighting Under Balcony

HCS Project Manager: Patrick McCord

Principal: Zack McQuigg

Architect: N/A

Contractor: Lightserve

Project Scope: The auditorium house lighting will be retrofitted. The new lights are LED and will be controlled by a new building automation control system. All of the down lights around the perimeter of the auditorium and all the pathway lights will also be retrofitted to LED.

Current Status: All the lighting retrofit work is complete. The commissioning of the system will be complete by the first week of August.

Budget: Original Contract: \$202,261.43



Budget Issues: None

Schedule: To be complete by August 2019



Schedule Issues: None.

Achievements: Excellent low maintenance lighting system for the Auditorium.
