


Quarterly Executive Summary
2019 Modular Classrooms at Multiple Schools
Q2 2019

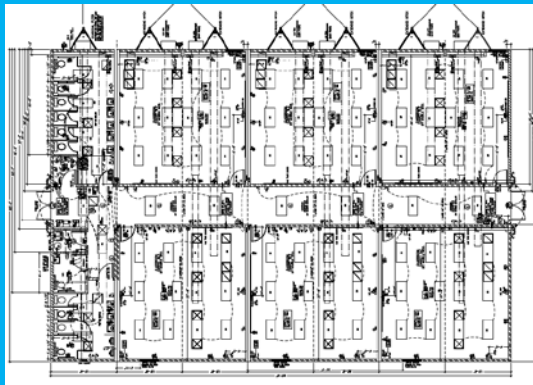

6-Classroom Unit with Restrooms Floor Plan

HCS Project Manager: Jason Hardee **Principals:** Rebecca Schroyer – OBES
Architect/Engineer: D. N. Engineering Vann Pennell - SJHS
Contractor: Mobile Modular Management

Project Scope: The following schools will receive modular classrooms for the 2019-2020 school year:

Ocean Bay Elementary School – Six (6) classroom modular building with restrooms.
St. James High School – Six (6) classroom modular building with restrooms.

Current Status: Modular classrooms are currently being delivered to both schools.

Budget: Original Budget: **\$1,935,368.00** Board Approved Date: **March 18, 2019**

Budget Issues: None at this time.

Schedule: Original solicitation: **June 13, 2016** (for annual modular purchases)
 Design completion: **April 25, 2019**
 Construction began: **June 10, 2019**
 Substantial Completion: **Expected August 15, 2019**

Schedule Issues: The earliest available OSF final inspection date is August 15, 2019.

Achievements: The modular classrooms began arriving onsite July 23, 2019, at SJHS and began arriving at OBES on July 24, 2019.
