


Quarterly Executive Summary
2019 Modular Classrooms at Multiple Schools
Q3 2019

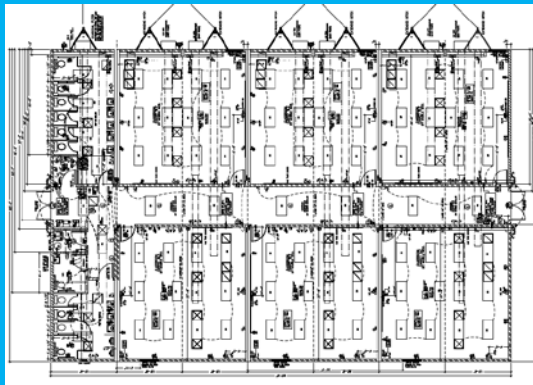

6-Classroom Unit with Restrooms Floor Plan

HCS Project Manager: Jason Hardee **Principals:** Rebecca Schroyer – OBES
Architect/Engineer: D. N. Engineering Vann Pennell - SJHS
Contractor: Mobile Modular Management

Project Scope: The following schools received modular classrooms for the 2019-2020 school year:

Ocean Bay Elementary School – Six (6) classroom modular building with restrooms.

St. James High School – Six (6) classroom modular building with restrooms.

Current Status: The modular classrooms have been installed and in use as designed. This will be the final report on this project.

Budget: Original Budget: **\$1,935,368.00** Board Approved Date: **March 18, 2019**

Budget Issues: None.

Schedule: Original solicitation: **June 13, 2016** (for annual modular purchases)
 Design completion: **April 25, 2019**
 Construction began: **June 10, 2019**
 Substantial Completion: **August 15, 2019**

Schedule Issues: None.

Achievements: The punchlist is complete and the projects have been closed out.
