


Quarterly Executive Summary  
Auditorium Lighting Retrofit – Myrtle Beach High School  
Q3 2019



New House Lights

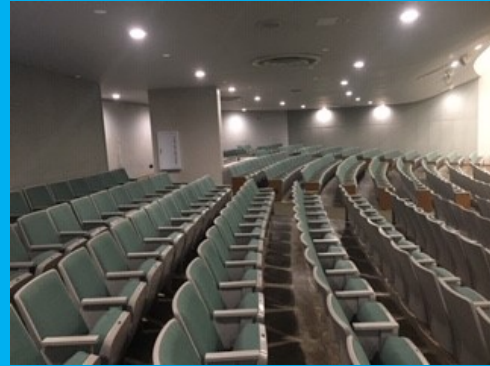

Lighting Under Balcony

**HCS Project Manager:** Patrick McCord

**Principal:** Zack McQuigg

**Architect:** N/A

**Contractor:** Lightserve

**Project Scope:** The auditorium house lighting has been completely retrofitted. The new lighting system is LED and is fully controlled by a new building automation system. All of the perimeter down-lighting in the auditorium and all pathway lights were also retrofitted to LED. All parties have been trained how to use the new system.

**Current Status:** All lighting retrofit work is now complete. The factory commissioning of the system was completed on September 25, 2019. This will be the final report on this project.

**Budget:** \$300,000.00

**Project Contract:** \$202,261.43



**Board Approved Date:** 1/29/2019

**Budget Issues:** None

**Schedule:** Completed



**Schedule Issues:** None

**Achievements:** Excellent low maintenance lighting system for the Auditorium.
