


Quarterly Executive Summary
Loop Road – Loris Middle School
Q3 2019

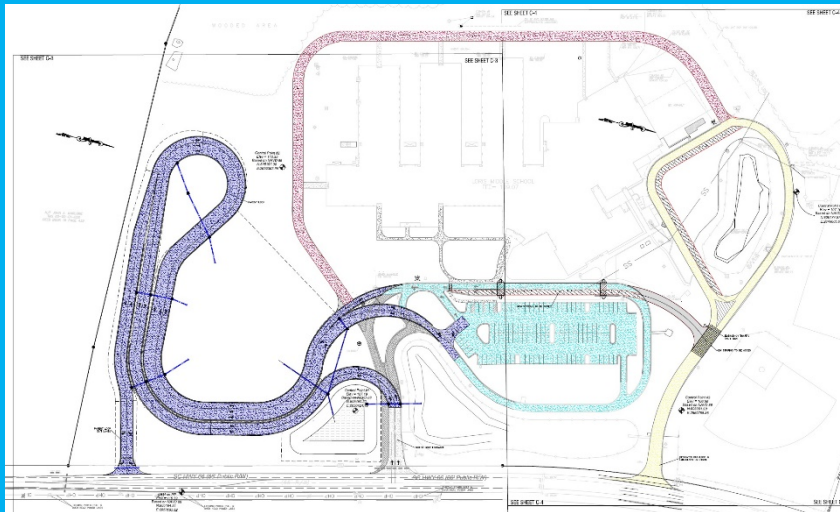

Project Manager:
Engineer:

Jason Hardee
Wall Engineering

Principal: Shelley Todd
Contractor: TBD

Project Scope:

Design and construction of a new parent drop-off loop road at Loris Middle School, for parent drop-off and pick-up traffic to reduce congestion on Highway 66 in front of the school.

Current Status:

Design and permitting is now 95% complete.

Budget:

Original Budget: **\$1,500,000.00** Board Approved Date: **1/29/2019**
Final Contract Amount: **\$ TBD**

Budget Issues:

None at this time.

Schedule:

Design: **In Progress**
Construction: **2020**

Solicitation: **November 2019**

Schedule Issues:

The procurement and construction phases have been delayed due to slow permitting and agency approvals at both the local and state levels.

Achievements:
